


Wastewater Utility 2018 Monthly Report



October 2018

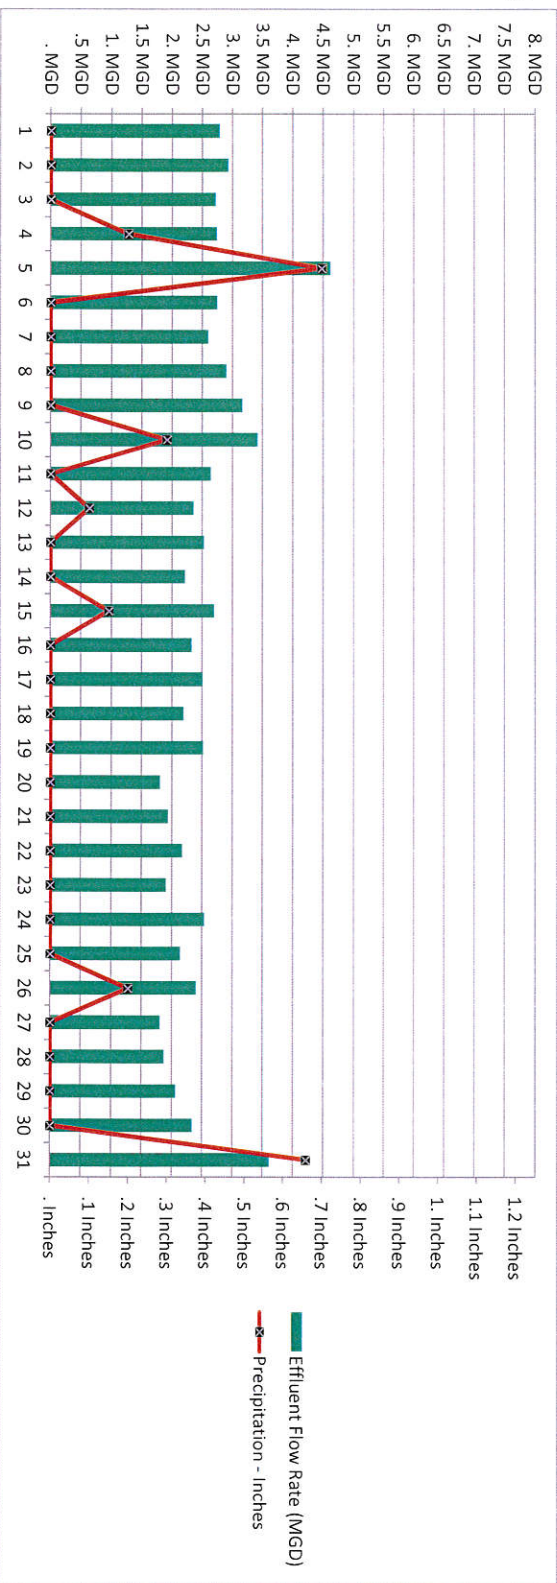

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2018	91.20	125.71	114.45	126.25	75.78	85.60	98.27	115.29	132.71	79.28	0.00	0.00	1044.54
Total MG Treated Effluent 2017	136.22	65.49	94.38	91.49	165.21	94.02	129.60	70.19	57.56	63.78	80.53	64.54	1113.01
Total Monthly Precipitation 2018	2.32	5.42	4.27	4.54	2.80	6.69	8.14	7.48	11.10	2.31	0.00	0.00	55.07

2018 Monthly Percent Capacity	73%	112%	92%	105%	61%	71%	79%	93%	111%	64%	0%	
Actual Design Flow 4.0 MGD												

Sewer Crew Activities

Catch Basins Repaired

Major Concrete Design

New Laterals Inspected

Major Projects Completed

Other Projects Completed

Emergency Repairs

Plant Crew Activities

Sludge Pressed / Gallons

Motors Repaired/Replaced

System Repairs

425 W. North , 4th & Penn, 310 S. Noble

The Old Concrete Dumping Station At The

Plant Was Modified To Fit Our New Vector

14 Homes

All Sewer Lift Stations Received Pump Oil

Changes And Electrical Checks (24)

Finished Grading And Clean-up At Meridian East Pond

As Well As Opening A Swale On Pippin Dr.

Poured Concrete Around Manhole And Fixed Driveway 1306 Bluebird Dr.

899,300

The #1 RAS Pump Came Back From Being Serviced

The #4 RAS Pump Was Sent In For Warranty Service / A Bad Seal

Plant Crews Installed A New Outdoor Light So That Our Night

Operators Could See Better Around The Circular Clarifier

Sludge Pump Compressors Required New Starters & Sensors

#3 Sludge Pump Had To Be Dismantled And Repaired
