


# Wastewater Utility 2019 Monthly Report



## May 2019

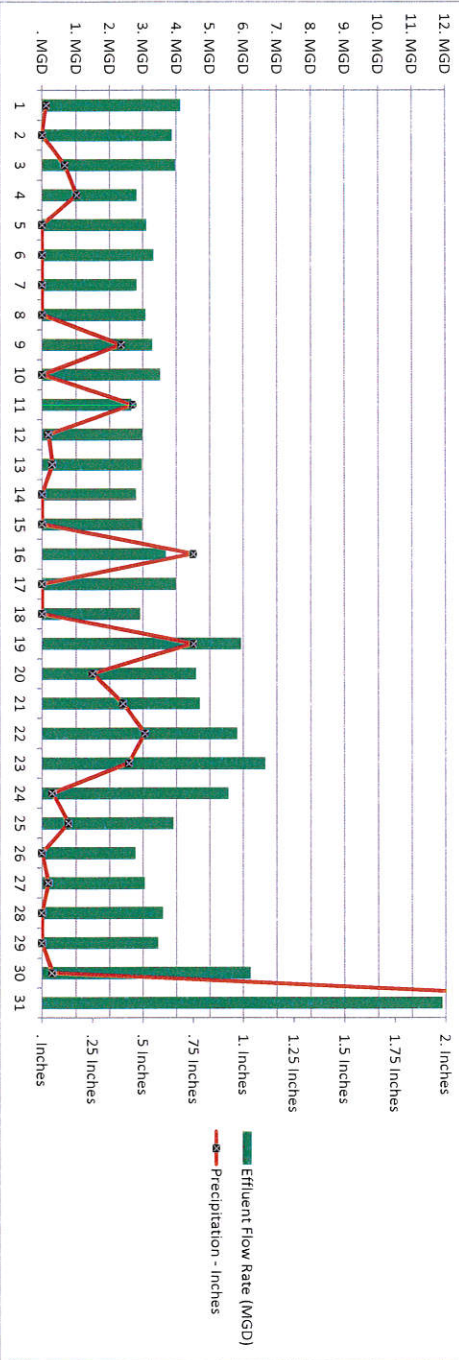

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2019	123.30	138.30	122.91	154.54	127.04								666.09
Total MG Treated Effluent 2018	91.20	125.71	114.45	126.25	75.78	85.60	98.27	115.29	132.71	79.28	120.06	97.73	1262.33
Total Monthly Precipitation 2019	2.24	6.52	4.89	6.58	7.77								28.00
2019 Monthly Percent Capacity	99%	123%	99%	129%	102%								
Actual Design Flow 4.0 MGD													

### Sewer Crew Activities

1. Performed 13 lateral inspections
2. Installed 205 feet of storm line
3. Repaired, replaced, or cleaned 13 storm structures
4. Cleaned 635' of sanitary and 5290' of storm
5. Replaced 3 laterals
6. Continued work on the OCRA program
7. Fixed force main at E. McClarron
8. Completed routine lift station maintenance

### Plant Crew Activities

Sludge Pressed / Gallons  
Plant Maintenance and Repairs:

1. Replaced/fixed flight boards in primary #2.
2. Continued repair work on the UV system.
3. New flow paced auto samplers were installed.
4. Ordered new travel bearings for Cemen Tech conveyor.
5. Nate assisting with work at the hospital water tower.
6. Working with Commonwealth on the compliance plan.
7. 10 loads of bio-solids hauled by Lawyer.
8. Replaced air intake filters on WWTP Blower #1, ordered more for #2 and #3.
9. Reported 3 violations for ammonia concentration, .2 for weekly average and 1 for monthly average.
