


Wastewater Utility 2019 Monthly Report



December 2019

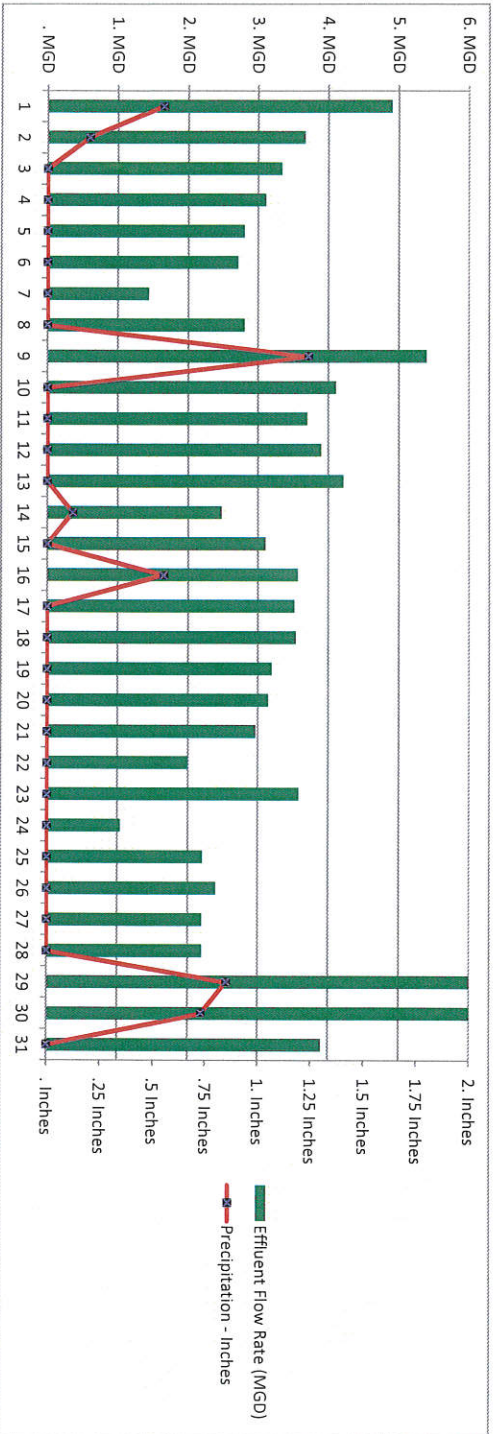

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2019	123.30	138.30	122.91	154.54	127.04	152.68	92.70	78.41	62.48	68.74	69.23	107.24	1297.57
Total MG Treated Effluent 2018	91.20	125.71	114.45	126.25	75.78	85.60	98.27	115.29	132.71	79.28	120.06	97.73	1262.33
Total Monthly Precipitation 2019	2.24	6.52	4.89	6.58	7.77	10.09	6.95	3.34	0.26	4.83	2.92	4.24	60.63
2019 Monthly Percent Capacity Actual Design Flow 4.0 MGD	99%	123%	99%	129%	102%	127%	75%	63%	52%	55%	58%	86%	89%

Sewer Crew Activities

1. Performed 16 lateral inspections
2. Completed routine maintenance and lift station checks.
3. Installed or repaired 2 private laterals under the lateral replacement program.
4. Cleaned/jetted 1200 feet of lines.
5. Repaired 2 catch basins.
6. Continuously clean catch basins to help prevent flooding during the rain events.
7. Root cut sanitary main from Douglas to Park on Swope St.
8. Finished Meridian Rd. storm project.
9. Responded to 7 service calls.

Plant Crew Activities

- Sludge Pressed / Gallons: 438,100**
- Plant Operations and Maintenance:**
1. Completed required monthly maintenance.
 2. Sludge feed pump failed: replacement ordered and will be installed in the next few weeks. Still have one operational.
 3. Polymer blending system failed. We are currently running on a loaned unit until we get a replacement.
 4. New blower for the aeration system was delivered. Maintenance project is scheduled to get underway in early February.
 5. Replaced the final effluent flow meter.
 6. Replaced heaters in plant buildings.
 7. Semi-annual preventative maintenance was completed on all generators.
