


Wastewater Utility 2020 Monthly Report



June 2020

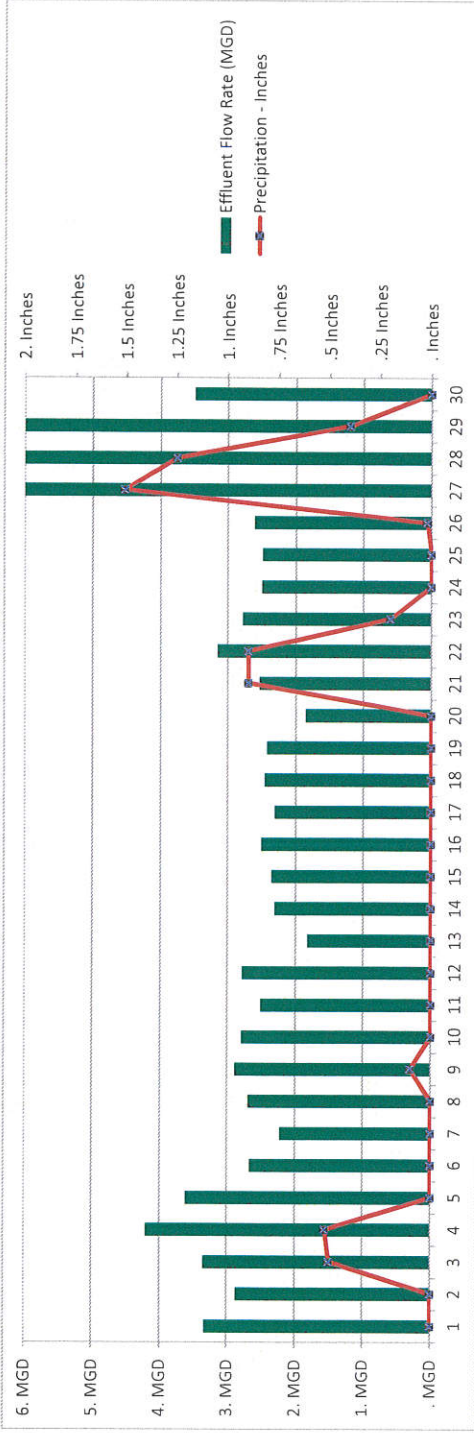

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2020	125.83	104.77	110.88	88.40	102.31	95.70	92.70	78.41	62.48	68.74	69.23	107.24	627.89
Total MG Treated Effluent 2019	123.30	138.30	122.91	154.54	127.04	152.68	92.70	78.41	62.48	68.74	69.23	107.24	1297.57
Total Monthly Precipitation 2020	6.12	5.26	4.51	1.92	4.95	6.30							29.06

2020 Monthly Percent Capacity	101%	90%	89%	74%	83%	80%							86%
Actual Design Flow 4.0 MGD													

Sewer Crew Activities

1. Performed 18 lateral inspections
2. Completed routine maintenance and lift station checks.
3. Cleaned 3675' of storm and sanitary lines.
4. Responded to 6 service calls
5. Cleaned and checked catch basins.
6. Replaced pump in the I-70 lift station.
7. Had a pump in Greenfield Village lift station fail: new pump has been ordered; also ordered extra pumps for Indigo, Fleming, and 2 as backup pumps.
8. Repaired/replaced 7 storm structures.
9. Made several repairs to sewer lines and a few lateral connections to eliminate some infiltration.
10. Replaced manhole structure and 20ft of pipe at North and Baldwin.
11. Conducted video investigations to locate inflow/infiltration.
12. The new collection system SCADA computer was delivered and put online.

Plant Crew Activities

Sludge Pressed / Gallons: 539,000

Plant Operations and Maintenance:

1. Completed required monthly maintenance.
2. Frakes Engineering replaced the HMI touch screen on belt press #2.
3. Had Armour Fire Protection check and inspect all fire extinguishers; had to replace and/or recharge a few.
4. Drained and cleaned final clarifiers.
5. Maintenance/Compliance project is moving along well; tanks 2, 3, and 4 are all back online; expect project to be complete by mid August.
6. Working on the design and layout of the new WWTP; layout has been finalized, now working on equipment and overall design. Expect to have preliminary design completed by late September or early October.
