


Wastewater Utility 2021 Monthly Report

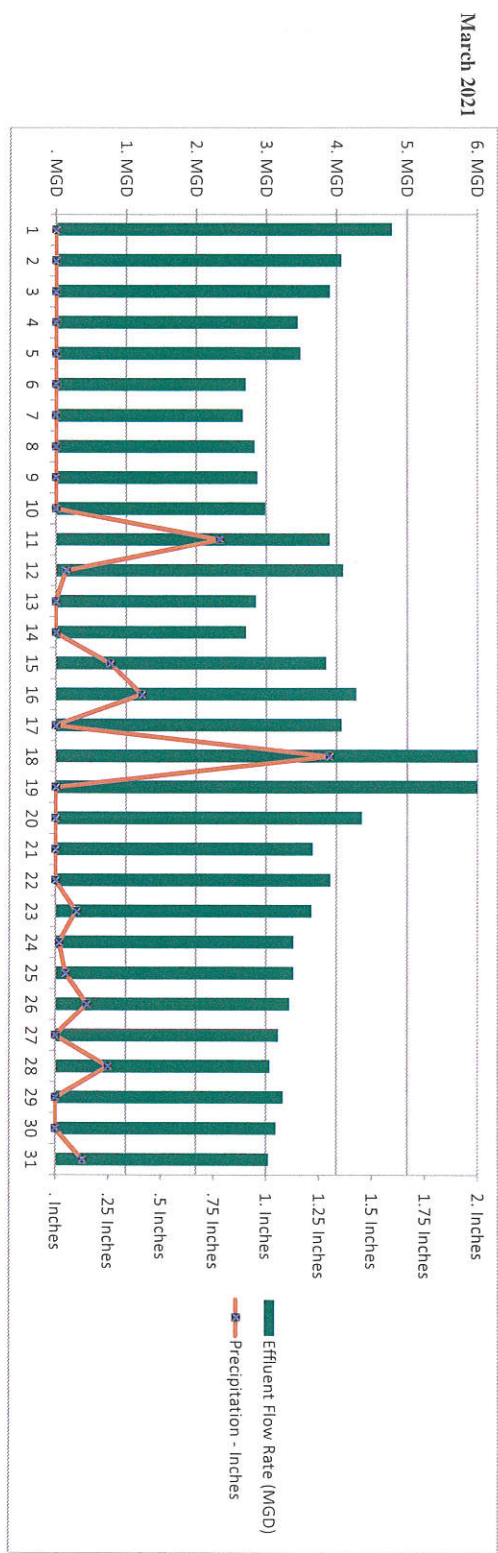

| Month | January | February | March | April | May | June | July | August | September | October | November | December | Total |
|----------------------------------|---------|----------|--------|-------|--------|-------|-------|--------|-----------|---------|----------|----------|---------|
| Total MG Treated Effluent 2021 | 93.67 | 91.88 | 123.06 | 88.40 | 102.31 | 95.70 | 82.61 | 83.06 | 64.78 | 80.31 | 90.43 | 83.15 | 308.61 |
| Total MG Treated Effluent 2020 | 125.83 | 104.77 | 110.88 | 88.40 | 102.31 | 95.70 | 82.61 | 83.06 | 64.78 | 80.31 | 90.43 | 83.15 | 1112.23 |
| Total Monthly Precipitation 2021 | 2.91 | 2.53 | 3.50 | | | | | | | | | | 8.94 |
| 2021 Monthly Percent Capacity | 76% | 82% | 99% | | | | | | | | | | 86% |
| Actual Design Flow | 4.0 MGD | | | | | | | | | | | | |

| Sewer Crew Activities | Sludge Pressed / Gallons: | Plant Operations and Maintenance: | Plant Crew Activities |
|--|---------------------------|--|-----------------------|
| <ol style="list-style-type: none"> Performed 27 lateral inspections Completed routine maintenance and lift station checks. Cleaned and/or CCTV'd 7402' of sanitary main lines and storm lines. Responded to 10 service calls; most were during a storm event on the 18th (flooding issues). Assisted water department with the install of new pumps at the south water plant. Installed repaired pump at Meridian Lift Station. Repaired sewer main at Spring and Douegas. Assisted with temporary repair of the mixing auger at the WWP and with the install of the new mixing auger. Assisted with the brush/tree removal in preparation of the road construction. Disconnected service lateral from old Animal Management office. Demolished/ore down old trailers at the Animal Management site. Cleaned storm catch basins multiple times in advance of heavy rains. Rebuilt 2 catch basins in St. James; replaced castings at Penn/Osage and Tague/Riley. | 846,300 | <ol style="list-style-type: none"> Completed required monthly maintenance. Hauled out 270 tons of bio-solids. Replaced the run timer on grit removal system (Pista Grit). Installed the new mixing auger on the Cemen Tech system. Buried the chemical supply conduits for the disinfection system (added protection from damage). Heavy rain / high flows caused the headworks building to flood; cleaned up once level was back to normal. Repaired roof-top exhaust fan on the Belt press Building (Cemen Tech side). Replaced 1 overhead door operator on the Belt Press building and had the others serviced. | |
