Wastewater Utility 2016
Monthly Report

October 2016

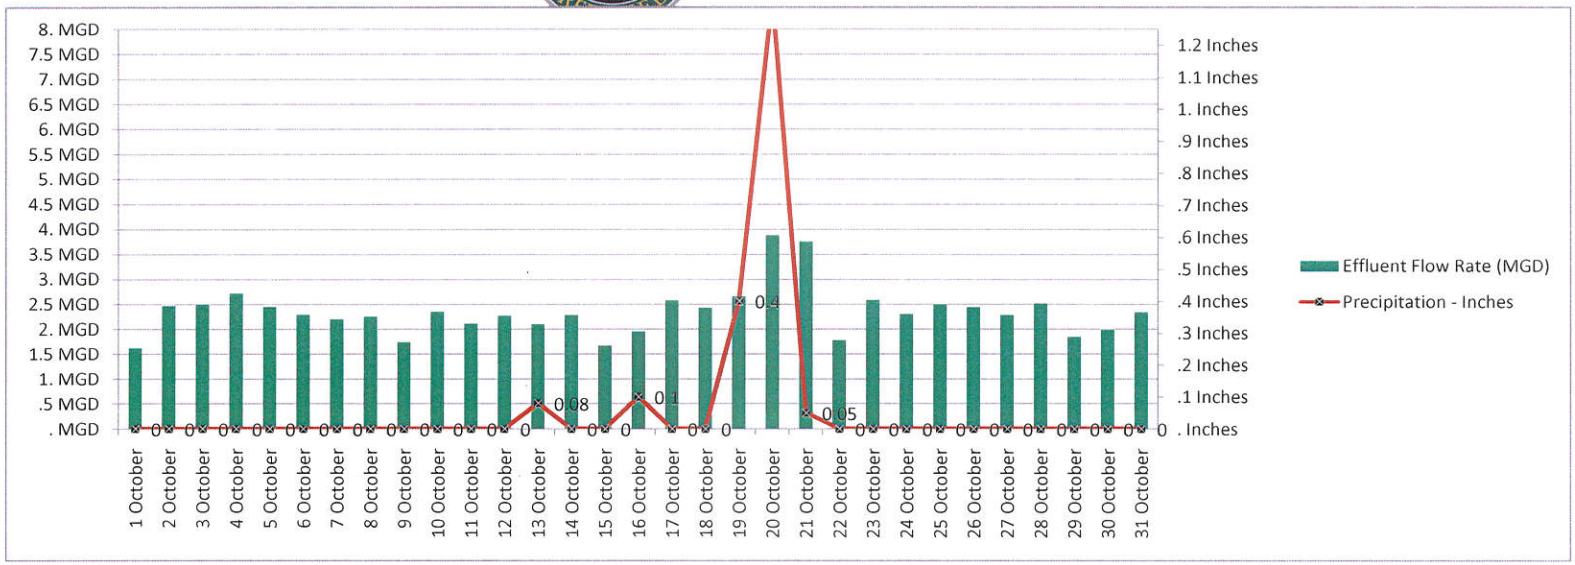

Month	January	February	March	April	May	June	July	August	September	October	November	December	Total
Total MG Treated Effluent 2016	100.67	95.46	124.48	119.42	98.65	78.16	77.60	109.48	88.08	73.17	0.00	0.00	965.17
Total MG Treated Effluent 2015	104.86	75.00	130.03	134.58	82.02	138.87	137.71	85.49	83.69	67.09	73.33	117.25	1229.92
Total Monthly Precipitation 2016	1.55	3.57	4.85	4.60	2.71	4.91	3.88	9.52	3.29	1.98	0.00	0.00	40.86

2016 Monthly Percent Capacity	81%	82%	100%	100%	80%	65%	63%	88%	73%	59%		
Actual Design Flow 4.0 MGD												

Sewer Crew Activities

Sanitary Sewers Cleaned / Ft.	2,493
Sewers Video Taped & GPS / Ft.	2,493
Sewer Cleaning and Videos	Completed Broadway / Monroe / W. 7th Street
Storm Sewers Cleaned / Ft.	Minimal
New Laterals Inspected	16 Homes
Major Projects Completed	Completed Bi-Annual Lift Station Maintenance & Hill Grove Sewer System Complete and On-Line
Catch Basin Installs / Repairs	Numerous Locations Throughout The City

Plant Crew Activities

Sludge Pressed / Gallons	628,300
Motors Repaired/Replaced	20 h.p. Compressor Motor for Sludge Pumps
The U.V. Disssinfection System Was Shut Down for Winter	
System Modifications	Worked With Kokosing Contracting To Install 2 Sludge Supernate Valves
Major Projects Completed	Installed the Last of Our New "Homemade" Concrete Walk Sections
